Southern New Hampshire University | School of Engineering, Technology, and Aeronautics

Monthly Status Report

[Team Thermocline]

Prepared by:	Team Thermocline
Date (MM/DD/YYYY):	03/15/2026
Reporting Period:	February 7th to March 15th

1. Project Status Summary % Complete (based on Project schedule)

	Green (Controlled)	*Yellow (Caution)*	*Red (Critical)*	*Brief Reason for Deviation*
Schedule	[ ]	[X]	[ ]	Testing procedures are becoming contingent upon completed fabrication.
Technical/ Scope	[ ]	[X]	[ ]	Some subsystem modifications made that digressed from our original design.
Budget	[ ]	[X]	[ ]	Manufacturing costs are using budget at expected rate. We are designing around our spending ability.

Explanation:

Schedule:
The team continues to stay on track to develop the system by the agreed-upon date in April. However, some critical milestones (such as testing procedures) are relying upon a completed system, and some project decisions are being made close to the deadline. But, large strides have been made by the team to conduct CAD reviews, submit large purchase orders, fabricate parts, and assemble the system. Most team assignments have been completed in a timely manner, with some having been allowed grace periods by the stakeholders. Nevertheless, the team has not encountered any major setbacks that will hinder the project timeline. The group plans on presenting the final system in April that meets the requirements. The schedule itself is often checked and updated accordingly, keeping the entire team accountable and efficient with their work.

Technical/Scope:
All aspects of the project are currently meeting the defined and derived requirements to satisfy the customer and relevant stakeholders. This month specifically, the group consulted with manufacturers, professors, and technical professionals to receive valuable feedback and improve the CAD and overall product design. Often was the design checked by the team to ensure risks are mitigated and the project meets the technical scope.

Budget:
The group continues to make financially-conscience decisions in reaching a more technical aspect of the project in designing and material/component purchasing. Many decisions have been made with the budget in mind, ensuring all fabrication and testing has the required pieces to be successful. The entire budget is actively tracked and managed, and all members are updated on its information.

2. Work Completed This Reporting Period

February 5th

“Quarter Board” was assembled and in the following weeks, underwent preliminary testing.

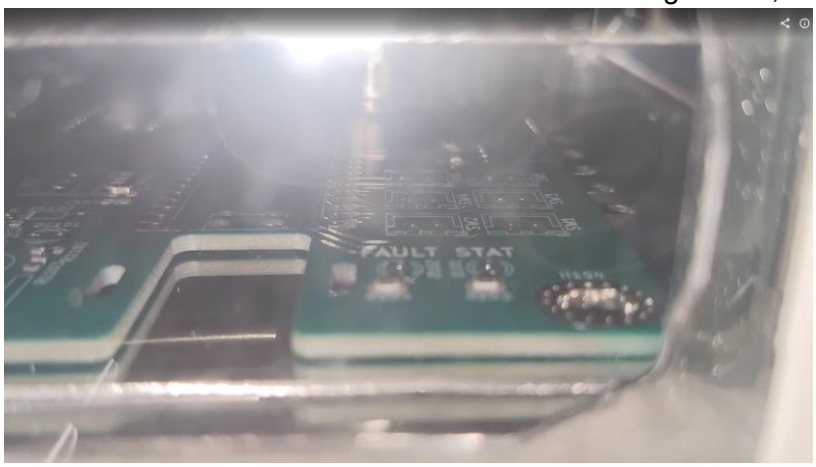

Also on Feb 4

Began 3d printing for test fit the Fan Panel and Heater Panels in 3d print and “CAD” (Cardboard)

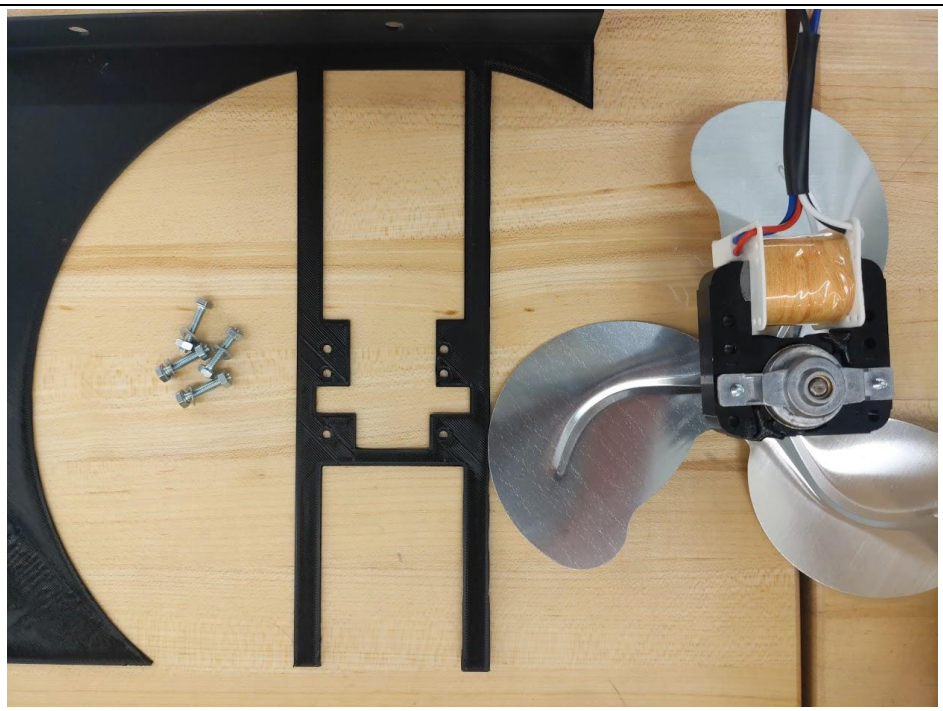

Feb 10

Board testing was complete.

Feb 14th

Offical CAD Review completed, we asked engineers and faculty for input on our design.

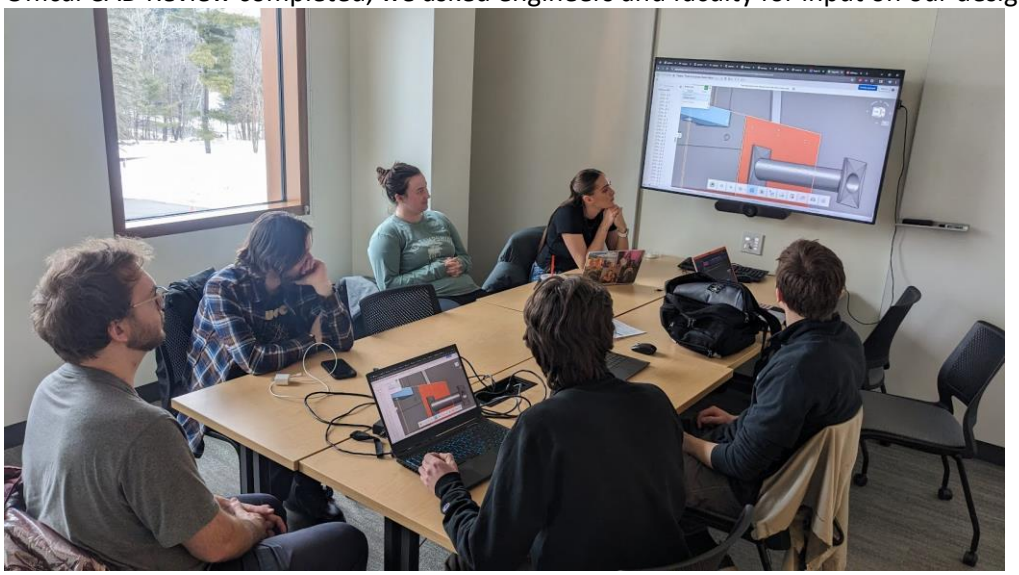

The first SCS order was also completed soon after.

Feb 19th

More “CAD” was completed, the entire internal section was mocked up in cardboard just before sendoff.

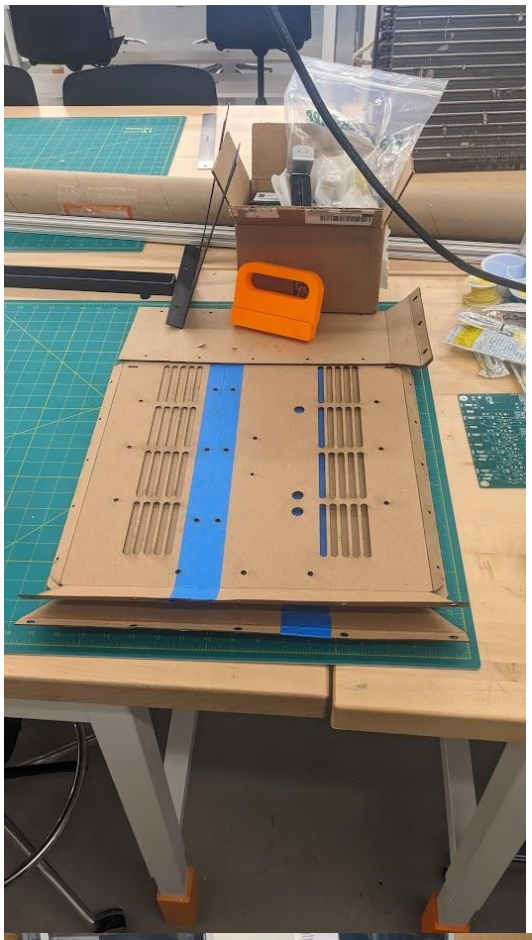

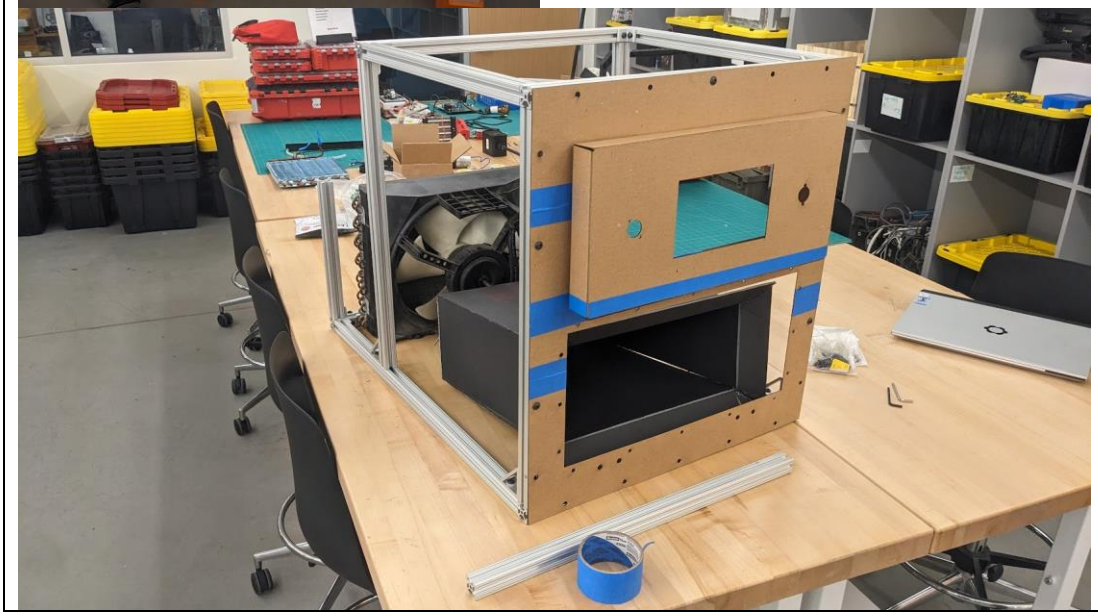

Feb 23

Final preparation of frame components are completed by joe at SMS machine shop in concord.

Feb 24

We have inter-thermal-team collaboration

Feb 25

The final full board is completed

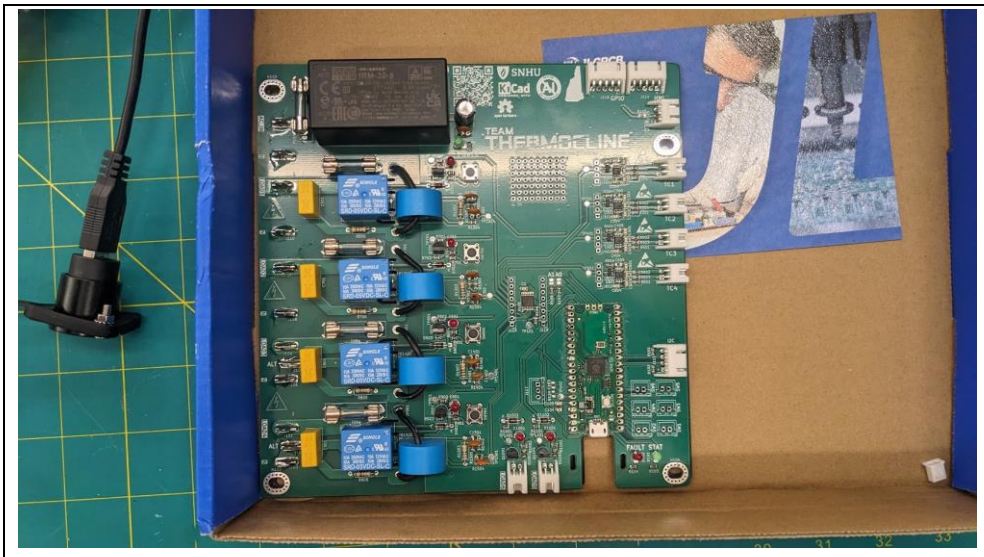

Feb 28

The UI is flashed and tested for function for the first time

March 9th

The first SCS order arrives

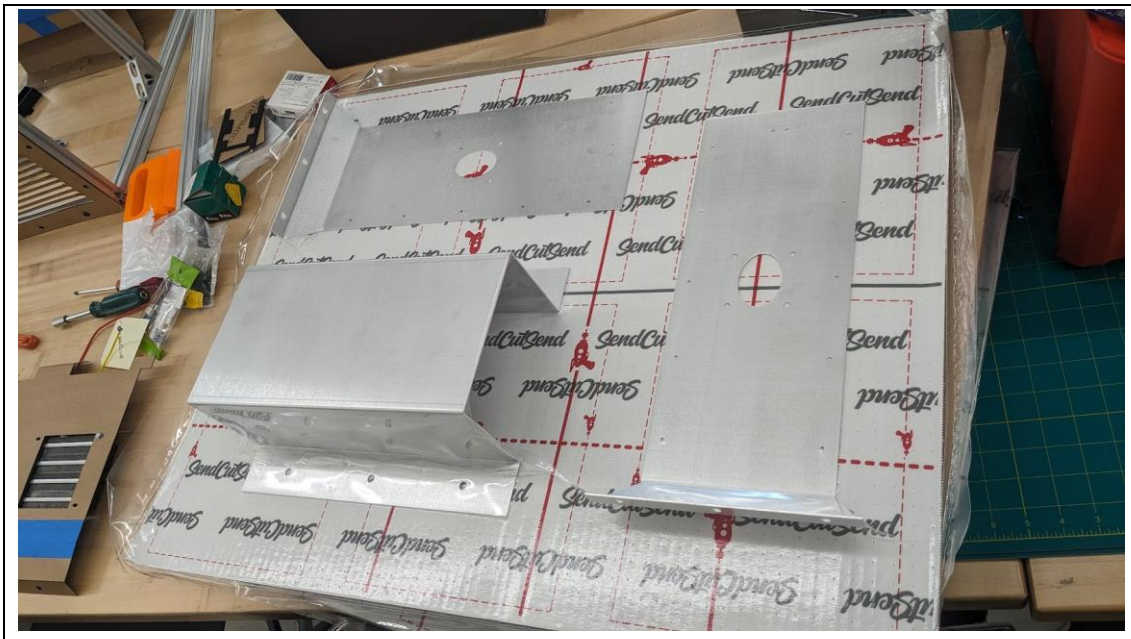

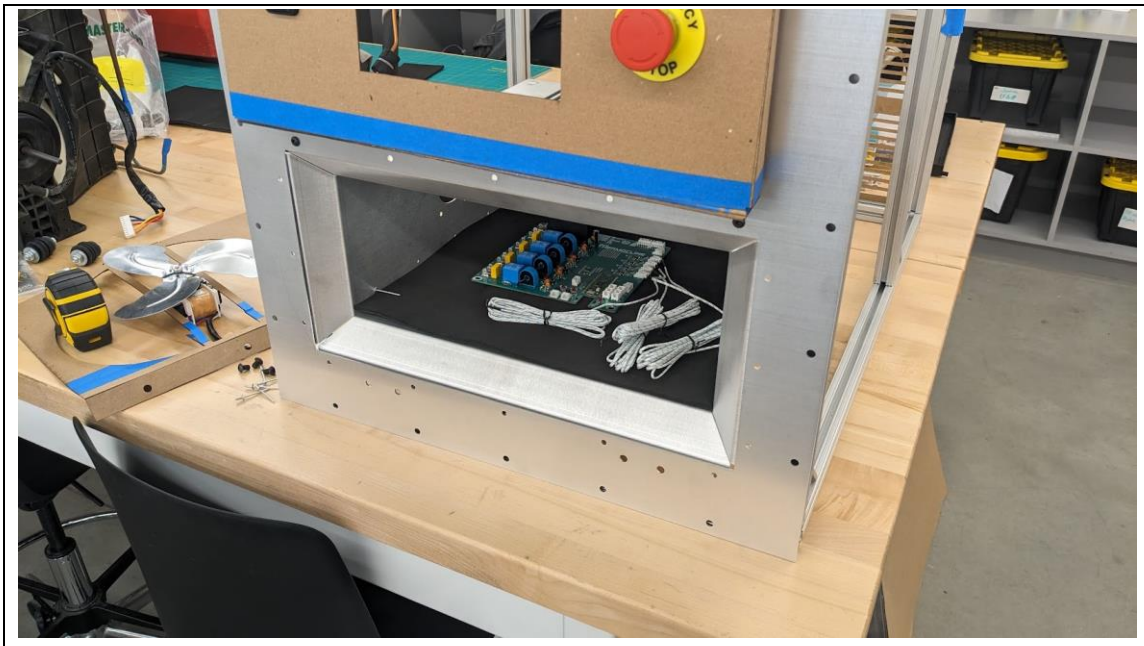

Mar 11

Gasket kits are made

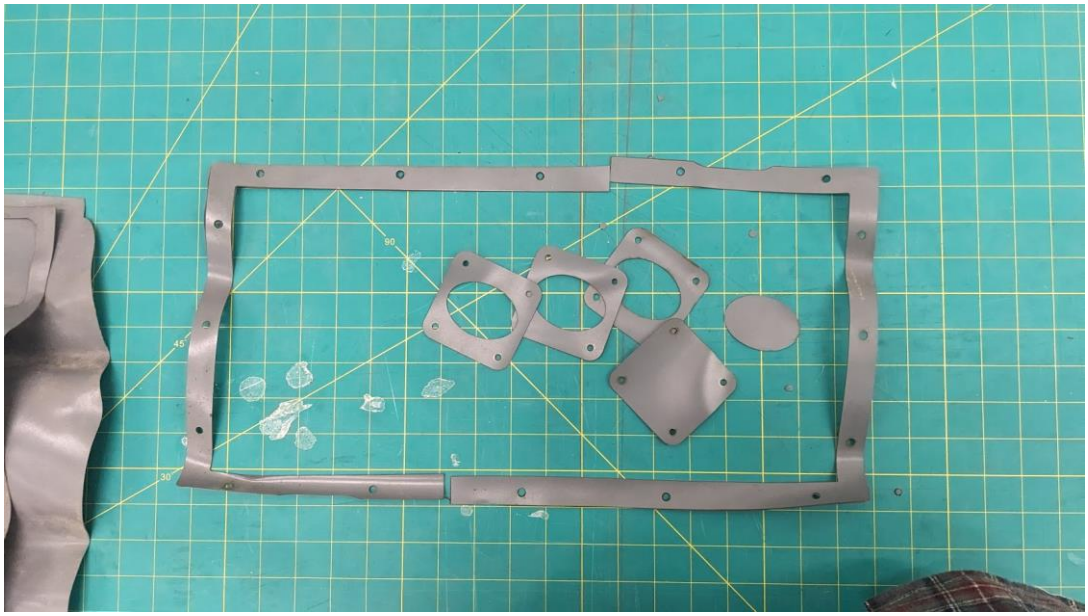

Also we collect RTV and insulation at home depot

Mar 12

The team assembles the interior structure

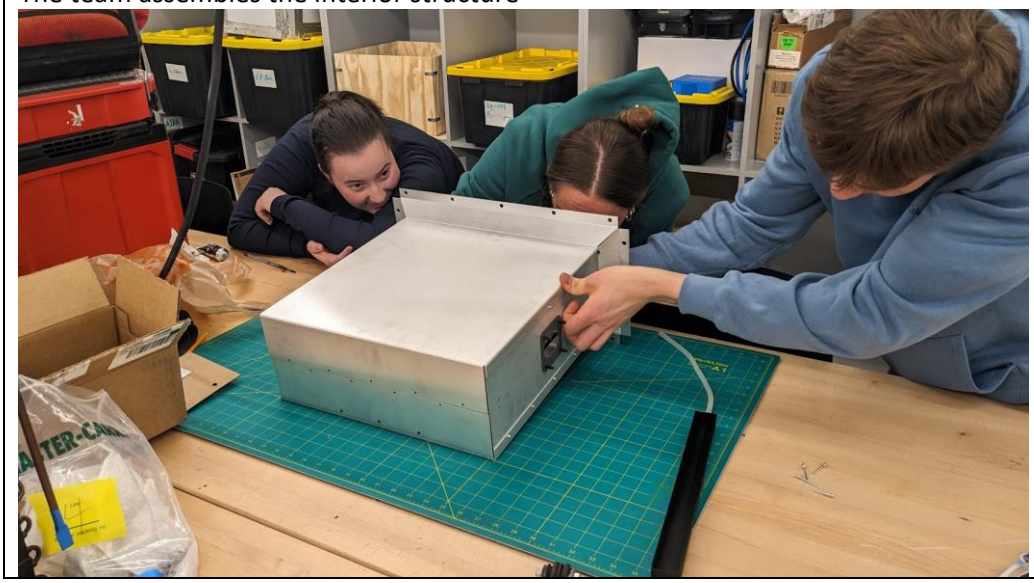

Mar 13

We make a custom rivnut tool

Mar 14

The volumes of the evaporator and condenser are measured

Also on that day, the passthrough blocks are machined

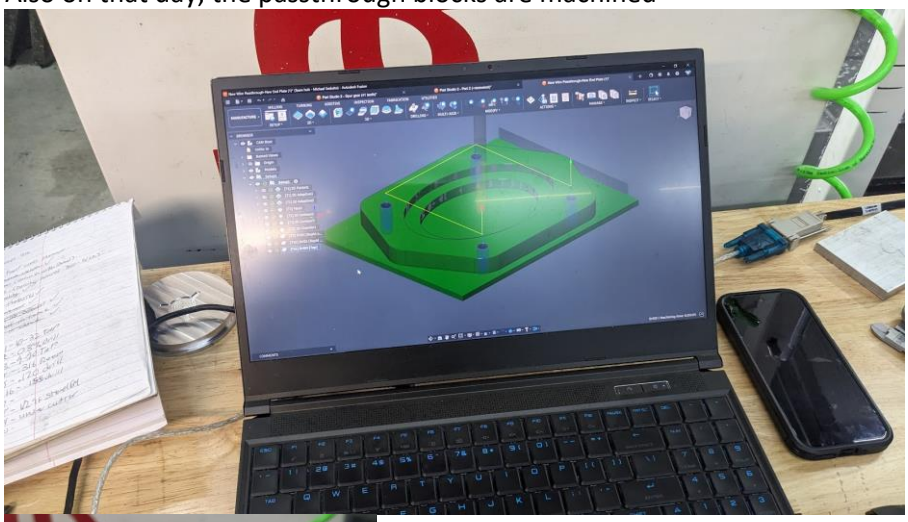

3. Deliverables/Milestones This Reporting Period

Aside from the above-listed work, the following milestones also occured:

- V1.0 board files
- Week 20
- LCSC Order
- PTRR
- SCS Order 2
- SCS Order 3
- Miscellaneous mechanical parts order
- System Operational Description (individual assignment)
- Functional Test Procedure
- Peer Evaluations

4. Open Issues and Mitigation

The following list outlines current project issues and team plans for mitigation.

- As we approach our budget max, we need to constantly be thinking about ways to save money and avoid costly off-site manufacturing.
- Ensuring the team has the necessary equipment on-site for final fabrication and testing procedures. Will hold a team-discussion to research appropriate equipment and speak with the necessary personnel at SNHU.
- Keeping all members up-to-date on individual/collective project goals, holding accountability in tasks, and ensuring all members have a solid share in project contributions. Will discuss with the team to develop a document or plan to track and manage these.

5. Budget Report

Expense	Original Budget [$]	Spent to Date [$]	Balance Remaining [$]	Estimate at Completion [$]
Mechanical	2000	1363.76	636.14.05	1,750
Electrical	500	546.91	-46.91	546.91
Management Reserve	600	0	600	103.09
Other (Tools, Equipment)	600	503	97	600
Total	3,000	2413.67	586.33	3000
Comments:				

6. Deliverables/Milestones Next Reporting Period

Milestones (include major deliverables)	Approved Schedule	Current Forecast	Status
Final Frame and Body Assembly	3-24-26	3-24-26	In Progress

First Load Test	3-31-26	3-31-26	In Progress
Final Insulation and Packaging	3-31-26	3-31-26	Not Started
Final Testing	4-7-26	4-7-26	Not Started

7. Project Monthly Status Report/Signatures

Project Manager:	**Joseph Sedutto**

I have reviewed the information contained in this Monthly Status Report and agree.

Name (Team Member)	***Title (If applicable)***	***Signature***	***Date***
Jacob Morrissette	Chief Analyst	Jacob Morrissette	3-15-26
Joseph Sedutto	Program Lead	Joseph Sedutto	3-15-26
Nik DiLullo	Project Engineer	Nik DiLullo	3-15-26
Alexia Hnatowicz	System Engineer	Alexia Hnatowicz	
Alexandra Friebolin	Chief Test Engineer	Alexandra Friebolin	3-15-26
Supervisor	***Title***	***Signature***	***Date***

The signatures above indicate an understanding of the purpose and content of this document by those signing it. By signing this document, they agree to this as the formal Monthly Status Report document.
